


ID	Task Name	Duration	Start	Finish	2018	2019	2020	2021
1	Passaic River Tidal GRR (LPP)	829 days	Tue 5/1/18	Sun 7/4/21				
2	GRR APPROVAL	1 day	Tue 5/1/18	Tue 5/1/18				
3	Field Survey	60 days	Wed 5/2/18	Tue 7/24/18				
4	CONTRACT 1 - SOUTHWEST Plans & Specs	512 days	Wed 7/25/18	Thu 7/9/20				
5	Design Activities	512 days	Wed 7/25/18	Thu 7/9/20				
6	DDR - 30%	60 days	Wed 7/25/18	Tue 10/16/18				
7	P&S - 30%	60 days	Wed 7/25/18	Tue 10/16/18				
8	30% DQC review	20 days	Wed 10/17/18	Tue 11/13/18				
9	VE Study	30 days	Wed 11/14/18	Tue 12/25/18				
10	DDR - 90%	120 days	Wed 12/26/18	Tue 6/11/19				
11	P&S - 90%	120 days	Wed 12/26/18	Tue 6/11/19				
12	90% DQC, BCOES Reviews	20 days	Wed 10/2/19	Tue 10/29/19				
13	Contract 1 - Revised 90% for review	20 days	Wed 10/30/19	Tue 11/26/19				
14	90% ATR & IEPR Reviews	40 days	Wed 11/27/19	Tue 1/21/20				
15	Contract 1 - 100% DDR and P&S	40 days	Wed 1/22/20	Tue 3/17/20				
16	Real Estate Acquisition	132 days	Wed 10/2/19	Thu 4/2/20				
17	Railroad Coordination	320 days	Fri 1/11/19	Thu 4/2/20				
18	Contract 1 Advertise and Award	70 days	Fri 4/3/20	Thu 7/9/20				
19	CONTRACT 1 - SOUTHWEST Construction Activities	256 days	Thu 7/9/20	Sun 7/4/21				
20	Southwest Construction	12 emons	Thu 7/9/20	Sun 7/4/21				
21	CONTRACT 2 - I-95 Construction Activities	558 days	Wed 2/6/19	Sun 3/28/21				
22	2 - P&S - 90%	100 days	Wed 2/6/19	Tue 6/25/19				
23	90% DQC, BCOES Reviews	20 days	Wed 6/26/19	Tue 7/23/19				
24	Contract 2 - Revised 90% for review	20 days	Wed 7/24/19	Tue 8/20/19				
25	90% ATR & IEPR Reviews	20 days	Wed 8/21/19	Tue 9/17/19				
26	2 - 100% DDR and P&S	40 days	Wed 9/18/19	Tue 11/12/19				
27	Contract 3 Advertise & Award	70 days	Fri 12/27/19	Thu 4/2/20				
28	I-95 Construction	12 emons	Thu 4/2/20	Sun 3/28/21				
29	CONTRACT 3 - MINISH Construction Activities	430 days	Wed 2/6/19	Tue 9/29/20				
30	3 - P&S - 90%	100 days	Wed 2/6/19	Tue 6/25/19				
31	90% DQC, BCOES Reviews	20 days	Wed 6/26/19	Tue 7/23/19				
32	Contract 3 - Revised 90% for review	20 days	Wed 7/24/19	Tue 8/20/19				
33	90% ATR & IEPR Reviews	20 days	Wed 8/21/19	Tue 9/17/19				
34	3 - 100% DDR and P&S	40 days	Wed 9/18/19	Tue 11/12/19				
35	Contract 3 Advertise & Award	70 days	Fri 12/27/19	Thu 4/2/20				
36	Minish Construction	6 emons	Thu 4/2/20	Tue 9/29/20				
37	CONTRACT 4 - INTERIOR DRAINAGE P&S	758 days	Wed 7/25/18	Fri 6/18/21				
38	Interior Drainage Final Analyses	100 days	Wed 7/25/18	Tue 12/11/18				
39	DDR - 30%	100 days	Wed 7/25/18	Tue 12/11/18				
40	P&S - 30%	100 days	Wed 7/25/18	Tue 12/11/18				
41	30% DQC review	20 days	Wed 12/12/18	Tue 1/8/19				
42	VE Study	20 days	Wed 1/9/19	Tue 2/5/19				
43	DDR - 90%	170 days	Wed 2/6/19	Tue 10/1/19				
44	P&S - 90%	170 days	Wed 2/6/19	Tue 10/1/19				
45	90% DQC, BCOES Reviews	20 days	Wed 10/2/19	Tue 10/29/19				
46	Contract 4 - Revised 90% for review	40 days	Wed 10/30/19	Tue 12/24/19				
47	90% ATR & IEPR Reviews	20 days	Wed 12/25/19	Tue 1/21/20				
48	4 - 100% DDR and P&S	40 days	Wed 1/22/20	Tue 3/17/20				
49	Contract 4 Advertise & Award	70 days	Wed 3/18/20	Tue 6/23/20				
50	Interior Drainage Construction	12 emons	Tue 6/23/20	Fri 6/18/21				

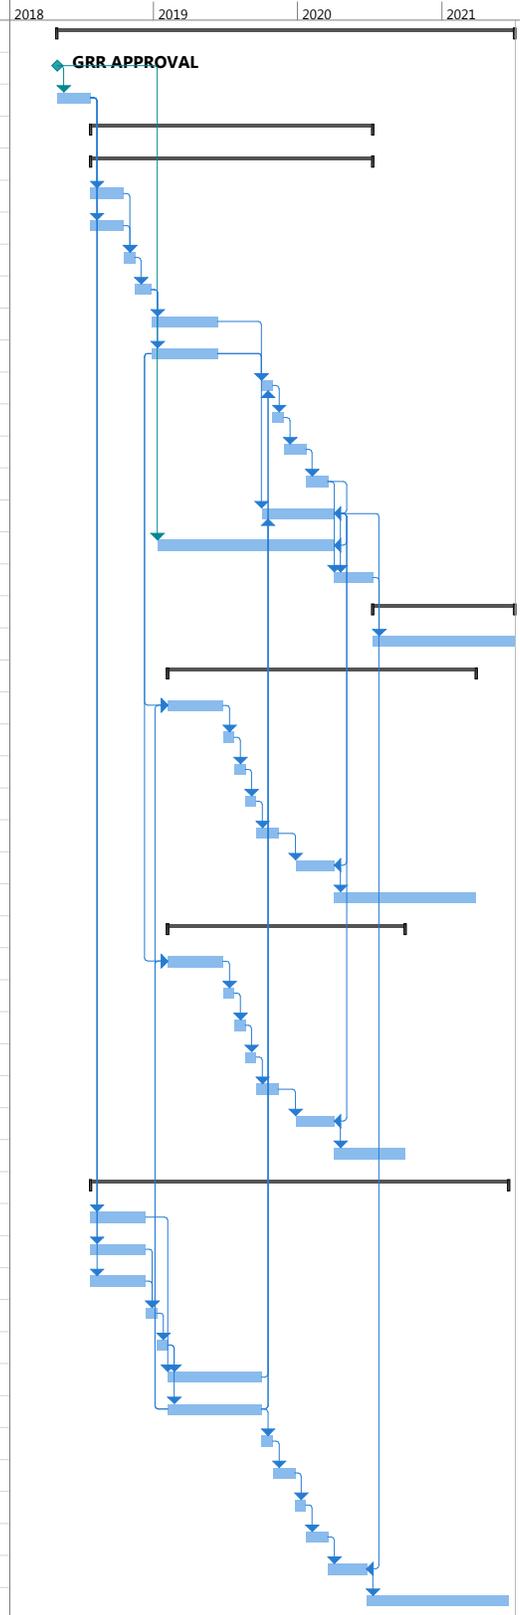

Project: PASSAIC TIDAL - Const	Task		Inactive Task		Manual Summary Rollup		External Milestone	
	Split		Inactive Milestone		Manual Summary		Deadline	
	Milestone		Inactive Summary		Start-only		Progress	
	Summary		Manual Task		Finish-only		Manual Progress	
	Project Summary		Duration-only		External Tasks			
